




2020 Street Improvements West Area (Contract 20-102) Construction Updates August 10, 2020

Phase and Schedule*

- Phase 1: April 20 - May 22
- Phase 2: April 27 - May 22
- Phase 3: May 4 - June 12
- Phase 4: May 11 - June 26
- Phase 5: June 8 - August 14

*Start and end dates subject to change.

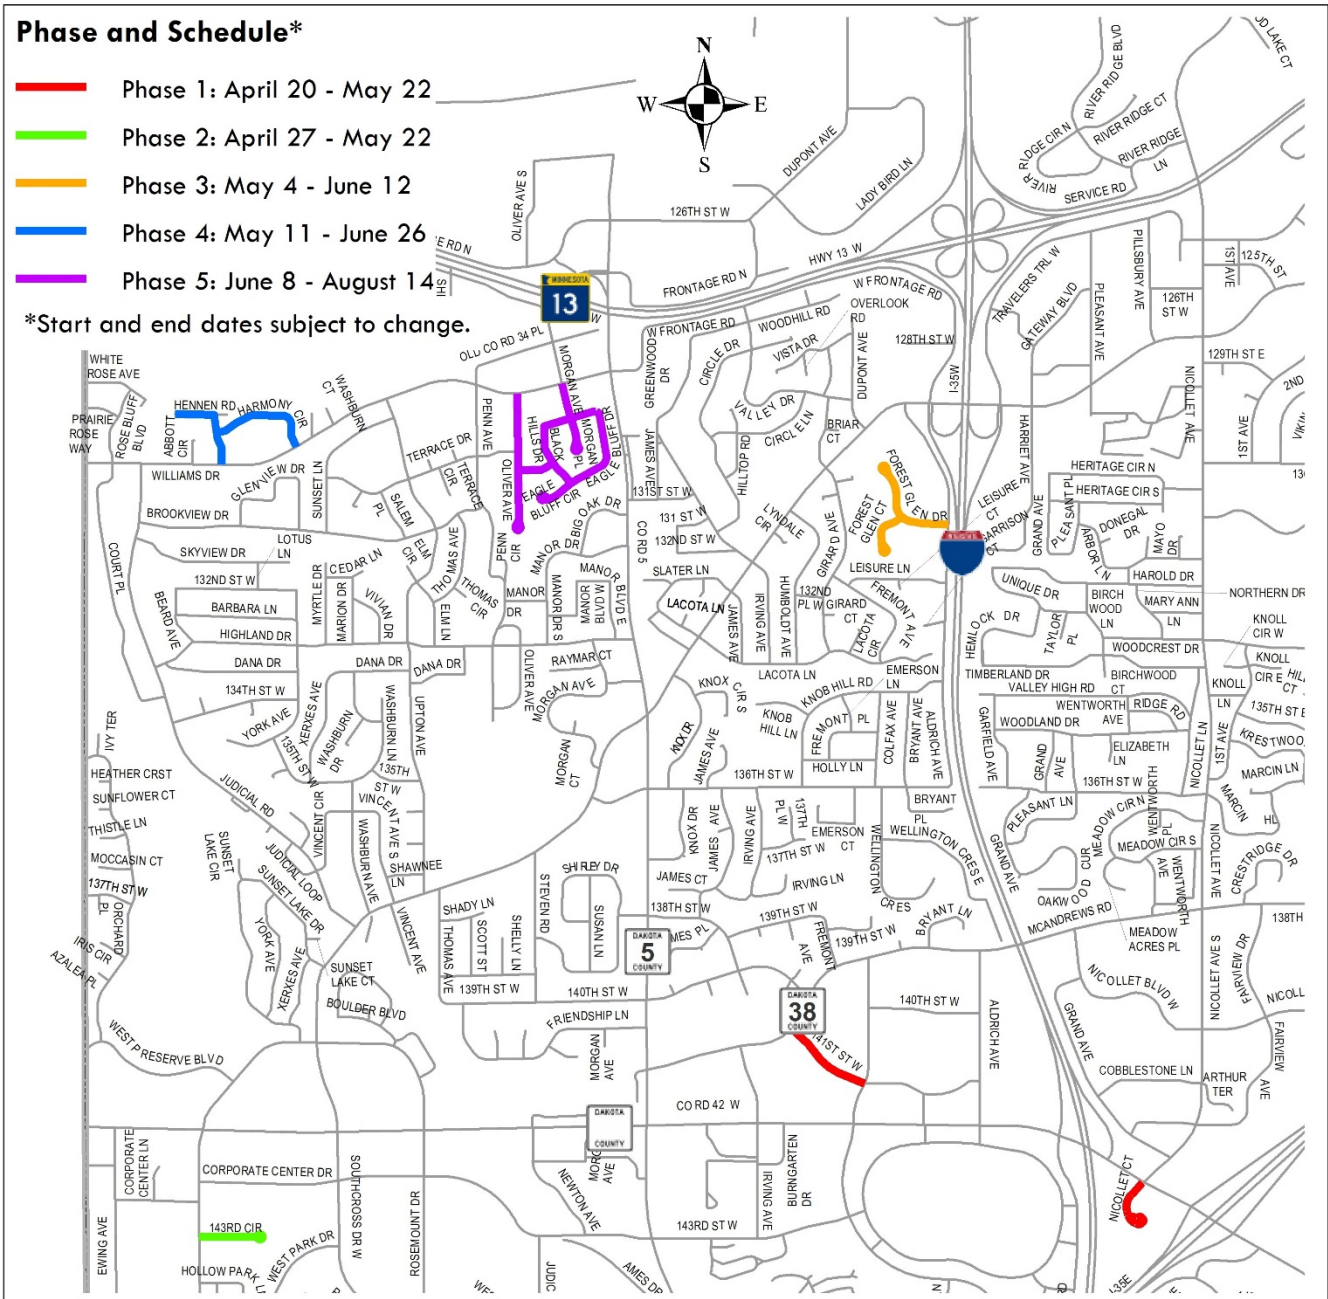

Date Saved: 4/29/2020 3:53:46 PM

Phase 1

Updates for the week of August 10-15, 2020:

- Continue replacing street signs

Looking ahead to the week of August 17-22, 2020:

- Finish replacing street signs

Phase 2 is Complete!

Phase 3

Updates for the week of August 10-15, 2020:

- Continue replacing street signs

Looking ahead to the week of August 17-22, 2020:

- Finish replacing street signs

Phase 4

Updates for the week of August 10-15, 2020:

- Continue replacing street signs

Looking ahead to the week of August 17-22, 2020:

- Finish replacing street signs

Phase 5







Updates for the week of August 10-15, 2020:

- Continue replacing street signs

Looking ahead to the week of August 17-22, 2020:

- Finish replacing street signs

2020 Street Improvements West Area (Contract 20-102) Estimated Schedule by Phase*

						
	Start	Utilities	Curb	Grading/Paving	Restoration	Complete
Phase 1	Apr 20	NA	Apr 20-24	May 4-8	May 11-21	May 22
Phase 2	Apr 27	NA	Apr 27 – May 1	May 6-8	May 4-15	May 15
Phase 3	May 4	May 4-5	May 5-12	May 13-21	May 22-Jun 12	Jun 12
Phase 4	May 11	May 11-15	May 26-29	May 25 – Jun 3	Jun 4-26	Jun 26
Phase 5	June 8	Jun 8-12	Jun 15-26	Jun 29 – Jul 17	Jul 20 – Aug 14	Aug 14

*Projected dates are subject to change based on weather and contractor operations.

Contact City Inspector Nils Hudyma at 612-619-5892 or nils.hudyma@burnsvillemn.gov for more information

Subscribe to email and text message updates!

Visit www.burnsvillemn.gov/roadwork and click the “Subscribe” button to sign up for email and/or text message updates.



Subscribe
